

Active

Adani Green Energy Limited (AGEL) Baiya

Baiya, Jaisalmer, Rajasthan [Open Map](#)

INTERNAL TOOLS

[Flight Hub 2](#)

[Spectra - Testing](#)

EXTERNAL TOOL

[Spectra - Production](#)

LAST UPDATED

[28 Aug 2026, 7:50 pm](#)

Site Details at a Glance

Total Capacity

600 MW


Total Blocks

51

Total ICRs

51

Site Map

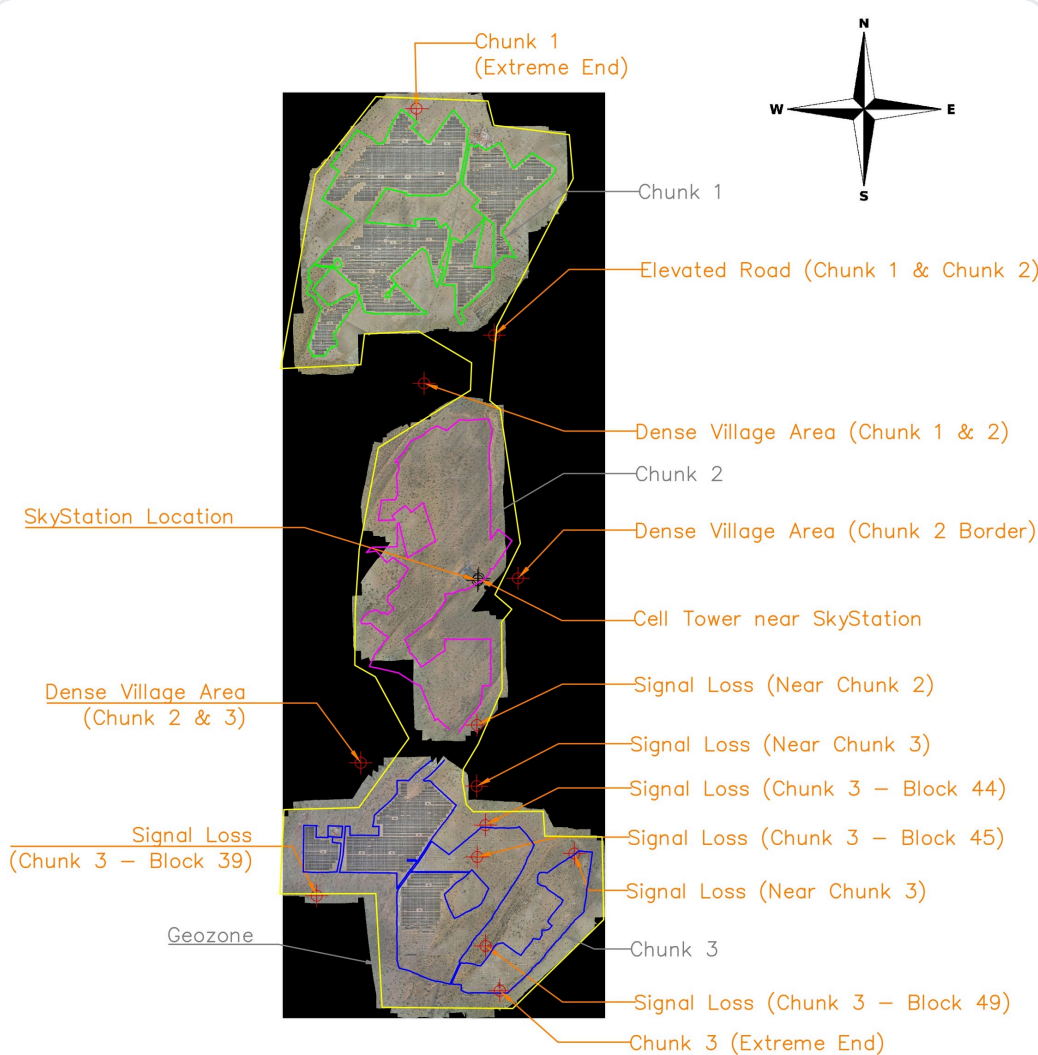

Need to Know



SkyStation Location
Near Chunk 2

Primary SkyStation location for site operations, flight planning, and overall operational reference.



Alternate Landing Point
15.2m away from SkyStation

Designated alternate landing location near SkyStation for emergency landing and recovery situations.



Relay Station
28.2 m away from SkyStation

Relay station associated with SkyStation, serving to solve signal blockage and achieve stable signal transmission.



Cell Tower
25.5 m away from SkyStation

Cell Tower; 25.5 m tower close to SkyStation; plan automated missions accordingly and maintain proper precautions during manual flight.



Dense Village Area
Between Chunk 1 & 2

Dense village habitation near Chunk 1 & Chunk 2 border area; strictly avoid flying over people and surrounding areas.



Dense Village Area
Near Chunk 2 Border

Dense village habitation near Chunk 2 border area; strictly avoid flying over people and surrounding areas.



Dense Village Area
Near Chunk 2 & 3

Dense village habitation near Chunk 2 & Chunk 3 border area; strictly avoid flying over people and surrounding areas.



Terrain Elevation Variation
Between Chunks 1 and 2

Sand dunes on elevated road between Chunks 1 & 2; account for terrain elevation during flight.



Night Inspection
Entire Chunk 1

High people movement and unauthorized-entry risk make Chunk 1 a priority area for night-time inspection.

Flight Parameters

Day Operations



Minimum Flight Altitude
Chunk 1

100 m



Minimum Flight Altitude
Chunk 2

100 m



Minimum Flight Altitude
Chunk 3

125 m



Maximum Flight Altitude
All Chunks

300 m



Safe Altitude
All Chunks

100 m



RTH Altitude
All Chunks

100 m

Night Operations



Minimum Flight Altitude
Block 12 to 17

80 m



Minimum Flight Altitude
Block 11

85 m



Minimum Flight Altitude
Block 10

100 m



Minimum Flight Altitude
Stockyard Area

120 m



Minimum Flight Altitude
Block 1 to 3

120 m

Flight Obstacles



Signal Loss - Chunk 3 (Block 45)
Signal Loss at 400 m with '112.0m' AGL



Signal Loss
Chunk 3 (Extreme End)



Signal Loss - Chunk 3 (Block 49)
Signal Loss at 280 m



Signal Loss - Chunk 3 (Block 34)
Signal Loss at 200 m with '105.1m' AGL



Sand Dunes - Elevated Road Between Chunk 1 & Chunk 2
Chunk 1 & Chunk 2 with '179m' ALT



Signal Loss
Chunk 1 (Extreme End)



Signal Loss - Chunk 3 (Block 51)
Signal Loss with '120.1m' AGL



Signal Loss - Chunk 2 (Block 33)
Signal Loss at 125 m with '100.1m' AGL



Signal Loss - Chunk 3 (Block 39)
Signal Loss with '104.1m' AGL



Signal Loss - Chunk 3 (Block 44)
Signal Loss at 300 m



Dock Health



Aircraft

Matrice 4 Series - 4TD



Battery Cycles

146 Cycles - Good



Dock Version

SkyStation 3



SkyStation Code

Baiya [Open Map](#)

Activities on Site

Construction Progress Monitoring

Work Site Monitoring

Inventory Progress Monitoring

Block Progress Monitoring

Wall Inspection

'ICR' Construction Progress Monitoring

Robot Installation Progress Monitoring

Night Security & Surveillance

Incident Log

Date & Time	Location	Incident Details	Action Taken	Log File
03 Jun 2026, 00:13:04	Near block 51	Drone initiated RTH after task completion and performed low-battery landing outside SkyStation landing area.	Drone was picked up back manually with the help of site team.	Open Log

Date & Time	Location	Incident Details	Action Taken	Log File
16 Jul 2026, 13:04:19	Near block 28	Drone did Emergency landing of it's own as battery was not enough to reach the SkyStation.	Obstacle sensors were cleaned, resolving false obstacle detection.	Open Log 

 Site Stakeholders

 DAY OPERATIONS

PERSON NO.	OPERATOR NAME	DESIGNATION
1	Kushagra	Drone Pilot
2	Sammith	Drone Pilot

 NIGHT OPERATIONS

PERSON NO.	OPERATOR NAME	DESIGNATION
1	Bishwajeet	Drone Pilot
2	Sree Ram	Drone Pilot

 ON-FIELD SUPPORT

PERSON NO.	PERSON NAME	DESIGNATION	CONTACT NUMBER
1	Mr. Vishal	Overall Site Head & IT Head	 +91 635894 7518
2	Mr. Jawant Bhati	Security Supervisor	 +91 72270 10549
