

Active

Tata Power Renewable Energy Limited (TPREL)

Kawaloor, Karnataka

Open Map

INTERNAL TOOLS

Flight Hub 2 (Global)

Spectra Testing

EXTERNAL TOOL

Spectra Production

LAST UPDATED

11 Sept 2026, 2:20 am

Site Details at a Glance

Total Capacity

350MW


Total Blocks

5

Total ICRs

5

Site Map

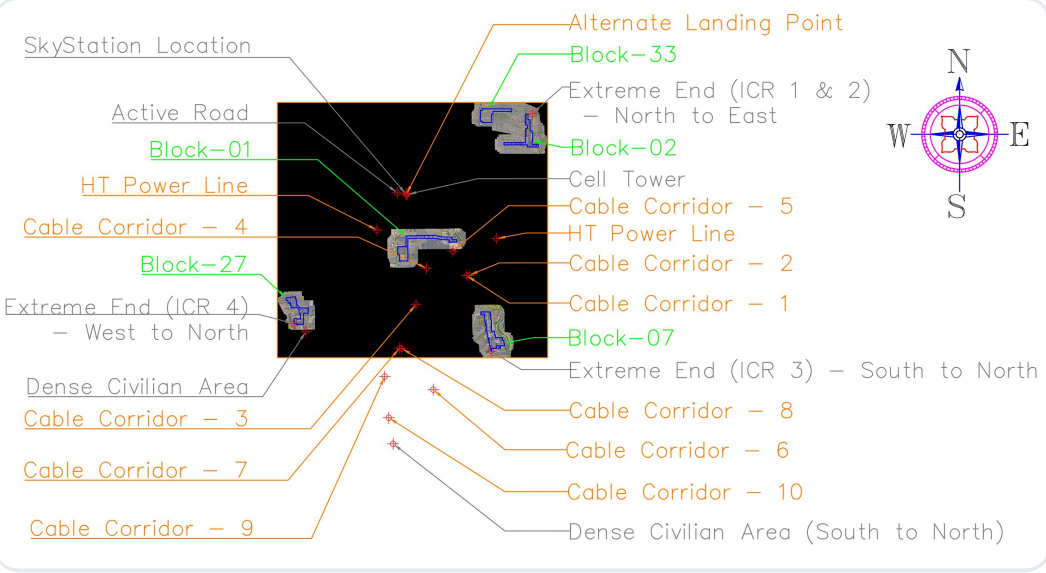

Need to Know

SkyStation Location

End of Block 09 corner

Primary SkyStation location for site operations, flight planning, and overall operational reference.

Alternate Landing Point

6.5 m away from SkyStation

Designated alternate landing location near SkyStation for emergency landing and recovery situations.

Cell Tower

33.8 m away from SkyStation

Cell tower is present at '33.8 m' away to SkyStation; plan automated missions accordingly and maintain proper precautions during manual flight.

Active Road near SkyStation

208 m from the SkyStation

Active road near SkyStation location with '208 m' distance away.

Extreme End (ICR 1 & 2) - North to East

SkyStation is ' 3462.4 m ' away; plan automated missions accordingly and maintain proper precautions during manual flight.

Extreme End (ICR 4) - West to North

SkyStation is ' 3964.9 m ' away; plan automated missions accordingly and maintain proper precautions during manual flight.

Extreme End (ICR 3) - South to North

SkyStation is ' 4054 m ' away; plan automated missions accordingly and maintain proper precautions during manual flight.

Dense Civilian Area

Besides 'ICR 4'

Dense civilian habitation at the end of the site near block '430' border area; strictly avoid flying over people and surrounding areas.

Dense Civilian Area

Between Block 36 & 39

Dense civilian habitation at the end of the site from block '1 & 2' border area; strictly avoid flying over people and surrounding areas.

Flight Parameters

Day Operations

Minimum Flight Altitude

All Blocks

80 m

Maximum Flight Altitude

All 5 Blocks

300 m

Safe Altitude

All 5 Blocks

80 m

RTH Altitude

All 5 Blocks

80 m

Night Operations

Minimum Flight Altitude

All 5 Blocks

40 m

Maximum Flight Altitude

All 5 Blocks

60 m

Safe Altitude

All 5 Blocks

50 m

RTH Altitude

All 5 Blocks

50 m

Flight Obstacles

Power Line

Hight Tension Power Line

Cable Corridor

Cable corridor Besides end of Block 418 for 25m

Cable Corridor

Cable corridor between Block 19 & Block 675 for 40m

Cable Corridor

Cable corridor near end of Block 566 for 30m

Cable Corridor

Cable corridor besides the Block 578 for 30m

Cable Corridor

Cable corridor opposite to Block 18 for 10m

Cable Corridor

Cable corridor near end of Block 650 for 10m

Cable Corridor

Cable corridor near end of Block 467 for 25m

Cable Corridor

Cable corridor besides Block 445 for 20m

Cable Corridor

Cable corridor near end of Block 467 for 25m (road side)

Cable Corridor

Cable corridor near end of Block 19 for 10m

Dock Health

Aircraft

Matrice 3 Series - 3TD

Battery Cycles

12 Cycles - Good

Dock Version

SkyStation 2

SkyStation Code

Koppal

Activities on Site

Construction Progress Monitoring

Work Site Monitoring

Inventory Progress Monitoring

Block Progress Monitoring

'ICR' Construction Progress Monitoring

Robot Installation Progress Monitoring

Night Security & Surveillance

Incident Log

No incidents recorded

Site Stakeholders

DAY OPERATIONS

PERSON NO.	OPERATOR NAME	DESIGNATION

1

Kushagra

Drone Pilot

NIGHT OPERATIONS

PERSON NO.	OPERATOR NAME	DESIGNATION
1	SreeRam	Drone Pilot

ON-FIELD SUPPORT

PERSON NO.	PERSON NAME	DESIGNATION	CONTACT NUMBER
1	Mr. Sourav Modak	Site Coordinator	+91 890463 4316
2	Mr. Raju	Night Ops Support	+91 974348 7365
3	Mr. Muthu G	Night Ops Support	+91 935345 3923
4	Mr. Yallappa G	Night Ops Support	+91 709021 7215
